

Hays County Commissioners Court



May 14, 2013



Hays County Commissioners Court

Pass Through Financing Program
Construction Update

May 14, 2013



PRIME
STRATEGIES,
INC.

HNTB



Projects in Design

Yarrington Bridge (at IH 35)

- Final PS&E at Division for review and approval
- Letting approved for August 2013


FM 1626 South (FM 2770 to FM 967)

- FHWA returned review comments
- Addressing review comments, anticipate revised document available for TxDOT in early June
- Awaiting TxDOT Comments on 60% PS&E
- Letting anticipated 2014





Precinct 1

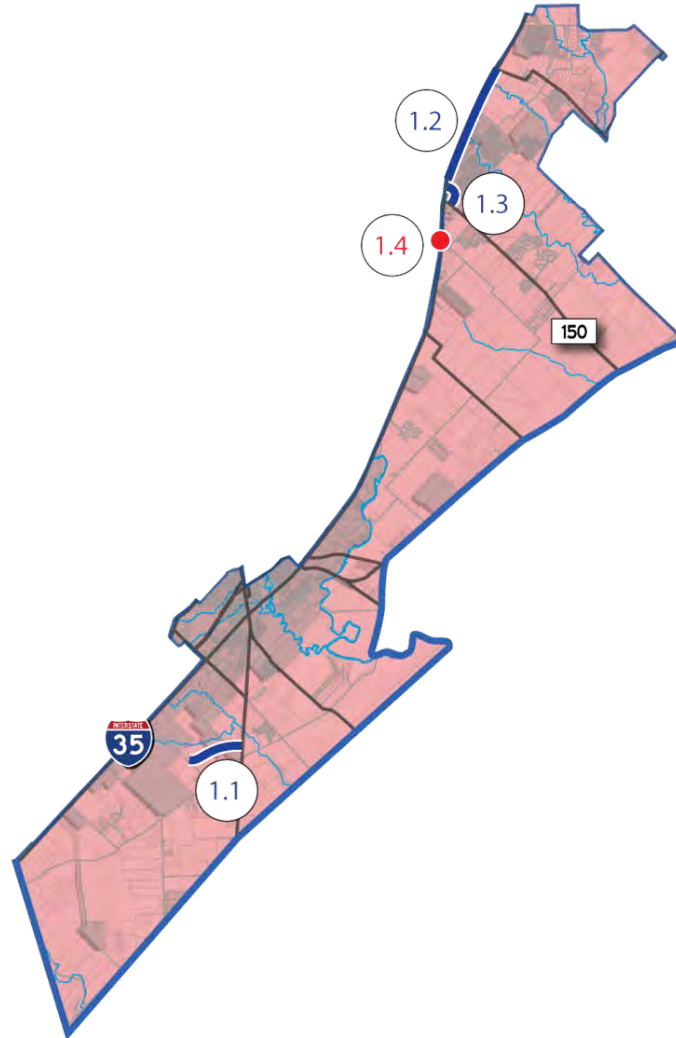

PRIME
STRATEGIES,
INC.

HNTB



IH 35 Phase 2A (RM 150 Realignment)

Anticipated Completion Date
Fall 2013



Original Contract Price = \$3,483,074.33

Total Executed Change Orders = \$47,586.88

Adjusted Contract Price = \$3,530,661.21

Work Completed to Date = \$2,175,833.11 (62%)



IH 35 Phase 2A (RM 150 Realignment)



Newly installed illumination poles and fixtures



IH 35 Phase 2A (RM 150 Realignment)



Finishing newly poured concrete median



IH 35 Phase 2A (RM 150 Realignment)



Pouring and finishing concrete sidewalk



FM 110 (McCarty Lane to SH 123)

Anticipated Completion Date
Late 2013



Original Contract Price = \$6,493,407.10

Total Executed Change Orders = \$0.00

Adjusted Contract Price = \$6,493,407.10

Work Completed to Date = \$2,700,082.96 (42%)



PRIME
STRATEGIES,
INC.

HNTB



FM 110 (McCarty Lane to SH 123)



Forming leveling pad for MSE Wall



FM 110 (McCarty Lane to SH 123)



Placing MSW Wall panels and bracing



FM 110 (McCarty Lane to SH 123)



Beginning first pass at mixing lime into subgrade




PRIME
STRATEGIES,
INC.

HNTB



Precinct 2

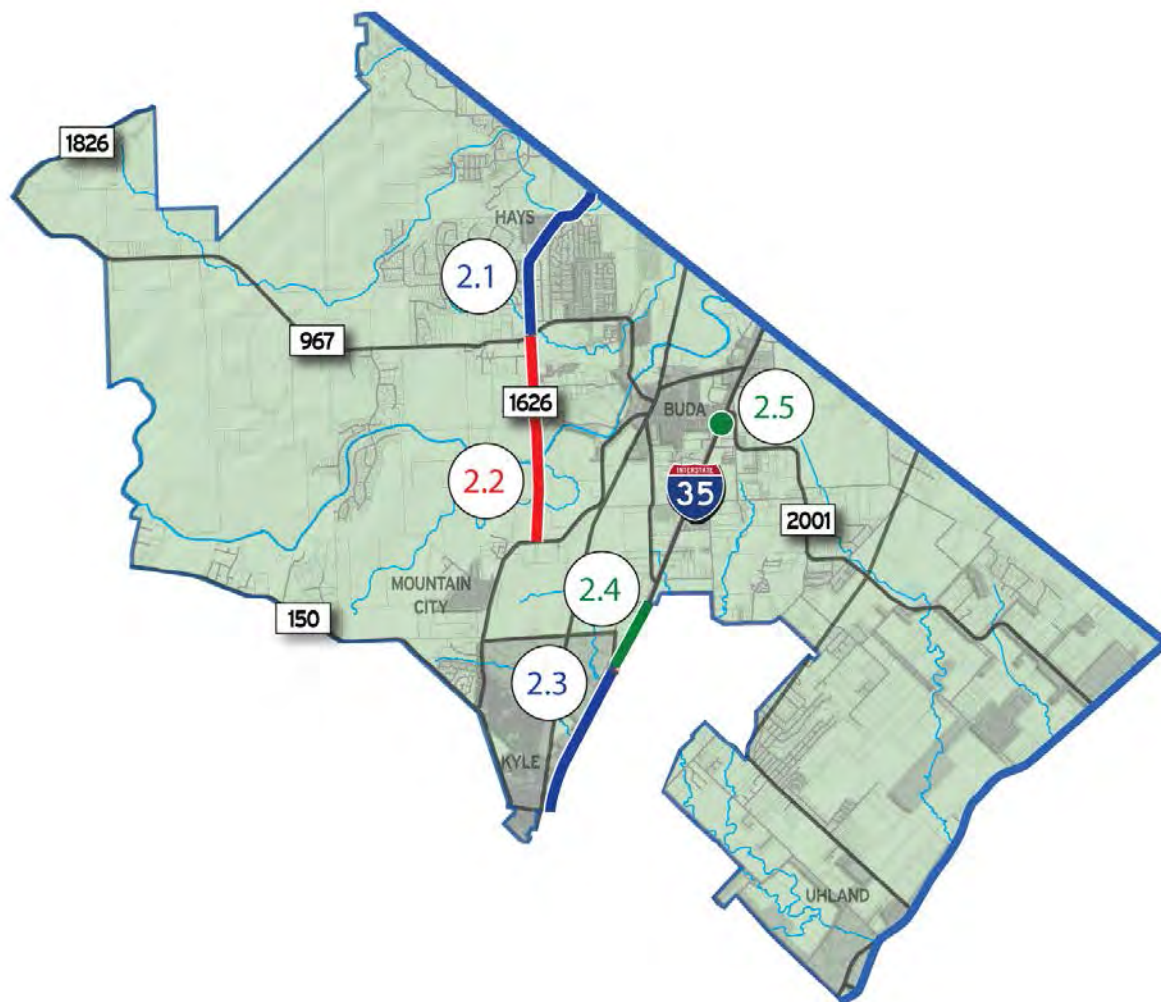



IH 35 Phase 2B (FM 1626 to Yarrington)

Anticipated Completion Date
Fall 2013



Original Contract Price = \$6,298,068.75

Total Change Orders to Date = \$18,667.86

Adjusted Contract Price = \$6,316,736.61

Work Completed to Date = \$4,760,546.96 (75%)



IH 35 Phase 2B (FM 1626 to Yarrington)



Excavation operations between frontage road and mainlanes



IH 35 Phase 2B (FM 1626 to Yarrington)



Button pavement markings installed on southbound frontage road



IH 35 Phase 2B (FM 1626 to Yarrington)



Upgrading metal beam guardrail to current standards



FM 1626 North (FM 967 to Brodie Ln)

Anticipated Completion Date
Fall 2014



Original Contract Price = \$17,235,782.15

Total Change Orders to Date = \$0.00

Adjusted Contract Price = \$17,235,782.15

Work Completed to Date = \$3,721,025.61 (22%)



FM 1626 North (FM 967 to Brodie Ln)



Setting bridge beams



FM 1626 North (FM 967 to Brodie Ln)



Forming extension and apron of Culvert B




FM 1626 North (FM 967 to Brodie Ln)



Pouring apron for Culvert E



Precinct 3

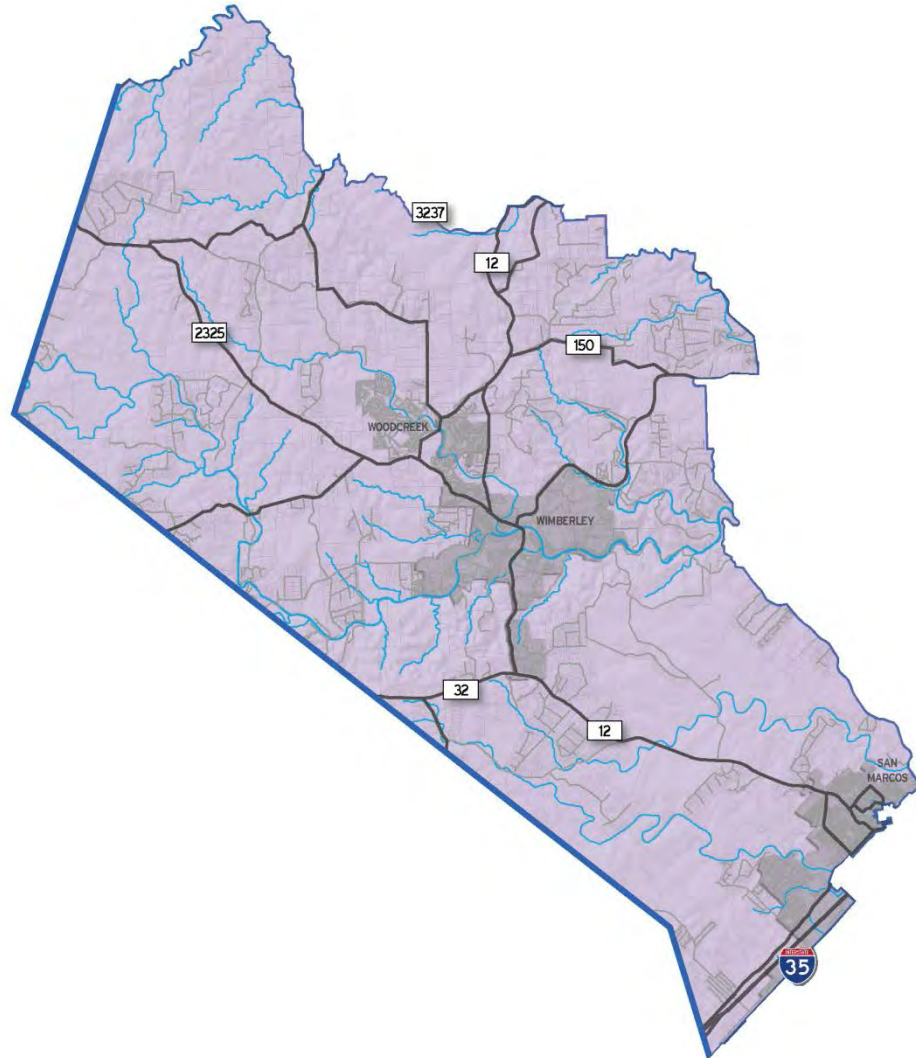


PRIME
STRATEGIES,
INC.

HNTB



Precinct 4

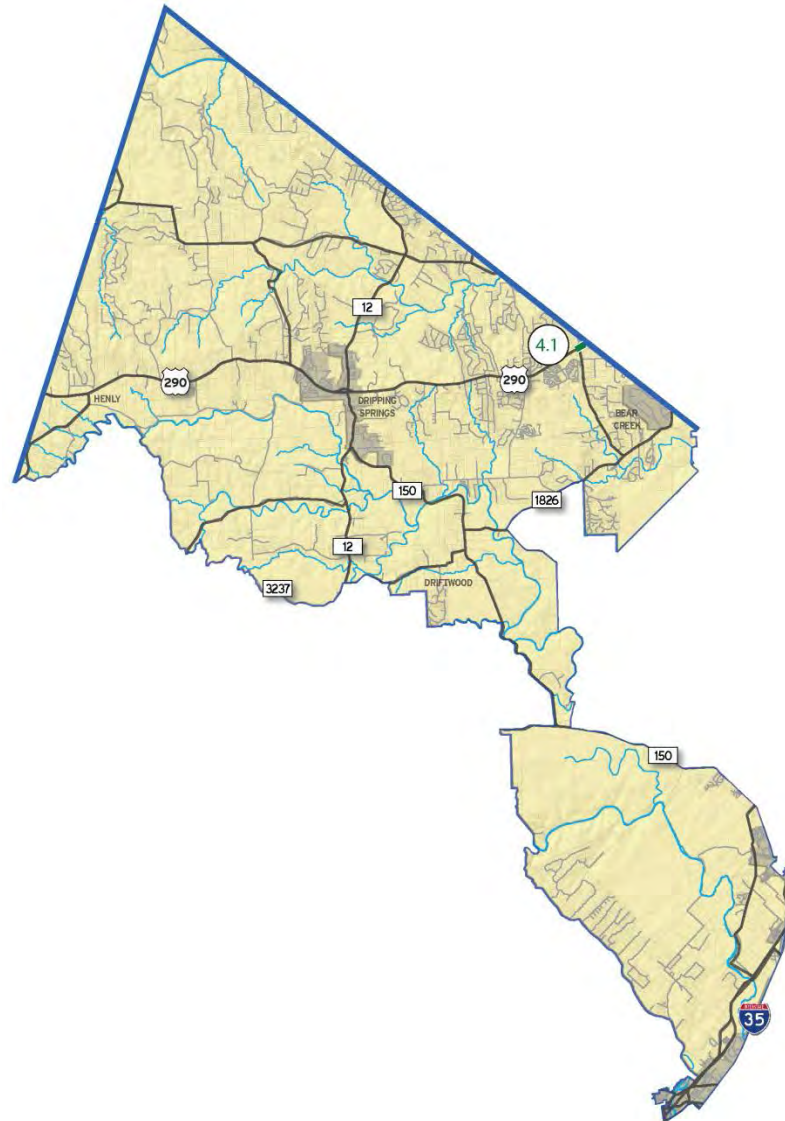

PRIME
STRATEGIES,
INC.

HNTB
